

abaa2025 building enclosure conference

ABAA Contractors Committee Panel Discussion: Submittal Risks and Responsibilities

Matt Giambrone
OCP Contractors

Michael Repka
Hoffman Construction

Corey Zussman
AECOM Hunt

Paul Grahovac
PROSOCO

AIA
Continuing
Education
Provider



Air Barrier Association of America (ABAA) is a Registered Provider with the American Institute of Architects Continuing Education Systems. Credit earned on completion of this program will be reported to CES Records for AIA members. Certificates of Completion for non-AIA members are available on request.

This program is registered with the AIA/CES for continuing professional education. As such, it does not include content that may be deemed or construed to be an approval or endorsement by the AIA of any material of construction or any method or manner of handling, using, distributing, or dealing in any material or product.



Contractors Committee Panel Discussion: Submittal Risks and Responsibilities

This interactive panel discussion will address shop drawing submittals and their role in construction. The speaker panel will have representative from legal, architectural, installer, and general contractor backgrounds who will discuss responsibilities of each party, and what risks each party may be talking on, knowingly or unknowingly. The panel will also discuss best practices for shop drawing creation, submission, and implementation in the field. Audience Q&A and participation is encouraged.



Learning Objectives

1. Understand the contractual requirements of shop drawings, and how they integrate with the contract documents.
2. Recognize potential risks/liabilities of shop drawings that modify design details.
3. Be able to define the role of the manufacturer in shop drawing creation.
4. Know the responsibilities of each party in submitting, approving, and implementing shop drawings



Michael Repka

AIA, LEED AP
Quality Manager
Hoffman Construction



Matt Giambrone

CABS
SPF Estimator and Project
Manager
OCP Contractors



Paul Grahovac

LEED AP
Director of New Business
Development, PROSOCO



Corey Zussman

*AIA, NCARB, ALA (IL, IN, WI) RBEC,
RRC, REWC, RWC, RRO, CABS, CDT
CQM, CxA+BE, BECxP, LEED AP BD+C
Level II Thermographer
QA/QC Vice President
AECOM Hunt*

Michael Repka

AIA, LEED AP

Quality Manager

Hoffman Construction

Michael joined Hoffman Construction Company 16 years ago after practicing architecture for 10 years in Seattle and the surrounding area. In his years of practice, he developed the firm's Quality Plan and executed internal Quality Reviews as a Project Architect, Project Manager, and Partner.

Michael has experience in many building types, high rise towers to below grade transit stations, and with GCCM and Design Build project delivery methods, as both an architect and contractor. A proud building science and sustainability geek, he completed the design and build of his own net-zero house in 2021

Matt Giambrone

CABS

SPF Estimator and Project Manager

OCP Contractors

Matt was born into the construction industry as his father successfully ran a masonry company in Cleveland, Ohio, for 35 years. Matt became an apprentice bricklayer in 2001, successfully completed training, and became a journeyman. In 2009, Matt studied blueprint reading and estimates by hand. In 2010, Matt became a Level 3 Certified ABAA installer in fluid-applied, self-adhered, and spray foam. With the passing of his father in 2013, Matt started at OCP Contractors, starting up their division 7 group. In 2016, Matt became the Chairman of the Contractors; a few years later, he became a Board of Director for the ABAA, and in 2021, Matt also became a member of the Executive Committee.

Paul Grahovac

LEED AP

Director of New Business

Development, PROSOCO

Paul Grahovac has been active in the construction industry for 30 years – first as a construction defects trial lawyer and later as corporate counsel and an expert in barrier technology. He also spent 10 years in technology development at a national lab.

Corey Zussman

AIA, NCARB, ALA (IL, IN, WI) RBEC,

RRC, REWC, RWC, RRO, CABS, CDT

CQM, CxA+BE, BECxP, LEED AP BD+C

Level II Thermographer

QA/QC Vice President

AECOM Hunt

As a forensic architect registered in several states, Corey Zussman has practiced in the construction industry for over 30 years. He specializes in the building envelope, restoration, preservation, life safety, and interior finishes. While working on over 2000 projects, Corey conducts constructability reviews, pre-installation meetings, comprehensive envelope meetings, and construction observations. He has also become known for providing educational opportunities throughout the industry and has produced more than 200 "lessons learned" papers. He is also a frequent presenter at local and national conferences and associations with over 50 AIA accredited presentations.

ABAA Contractors Committee Panel Discussion: **Submittal Risks and Responsibilities**

Shop Drawing Liability

AIA A201

§ 3.12.4 Shop Drawings, Product Data, Samples, and similar submittals are not Contract Documents. Their purpose is to demonstrate how the Contractor proposes to conform to the information given and the design concept expressed in the Contract Documents for those portions of the Work for which the Contract Documents require submittals. Review by the Architect is subject to the limitations of Section 4.2.7. Informational submittals upon which the Architect is not expected to take responsive action may be so identified in the Contract Documents. Submittals that are not required by the Contract Documents may be returned by the Architect without action.

Alloy
ARCHITECTURE

NO EXCEPTION TAKEN
 MAKE CORRECTIONS NOTED
 REJECTED
 REVISE & RESUBMIT

Checking is only for general conformance with the design concept of the Project and general information given in the Contract Documents. Contractor is responsible for coordination of his work with that of all other trades and for the satisfactory performance of his work.

By: GEOFF SNOW Date: _____

Catalyst Design Group, PC

REVIEWED
 REVIEWED AS NOTED
 REVISE & RESUBMIT
 REJECTED



No Exceptions Taken
 Note Markings
 Revise & Resubmit

Date: 11-18-2024
 By: [Signature]

Review is only for conformance with the design concept of the Project and compliance with the information given in Contract Documents. Contractor is responsible for dimensions to be confirmed and correlated at the

KINETIC
DESIGN + DEVELOPMENT

No Exceptions Noted
 Exceptions Noted
 Revise and Resubmit
 Rejected

NABHOLZ
Nabholz Construction
2223 W Sunset Street
Springfield, MO 65807
Ph: 417.450.6000

SUBMITTAL REVIEW

334100 Storm Utility Drainage Piping - Product Data

REVIEWED
 REVIEWED - EXCEPTIONS NOTED
 REVISE & RESUBMIT

Reviewed for general compliance with the Design Documents. Subcontractor or vendor is fully responsible for all material, accessories, coordination with Contract Documents and other trades, detailing, and field measurements, and related construction criteria necessary to produce a complete, properly functioning and coordinated product, prepared for installation in full compliance with the Contract Documents, Authorities having jurisdiction, and Nabholz Construction Corporation Subcontract or Purchase Order.

angele.baer
09/20/2024

This submittal has been reviewed for general conformance with the Contract Documents. Contractor review does not relieve the Vendor/Subcontractor of responsibility for compliance with all requirements of the contract, including completeness and accuracy of this submittal.

Reviewed / exc

CHECKING IS ONLY FOR GENERAL COMPLIANCE WITH THE DESIGN CONCEPT OF THE PROJECT AND GENERAL INFORMATION GIVEN IN THE CONTRACT DOCUMENTS. CONTRACTOR IS RESPONSIBLE FOR COORDINATION OF HIS WORK WITH THAT OF ALL OTHER TRADES AND FOR THE SATISFACTORY PERFORMANCE OF HIS WORK.

Reviewed by: Michael Fletcher Date: 08/21/2024

Barge Design Solutions

sequences of procedures. The Architect's approval of a specific item shall not indicate approval of an assembly of which the item is a component. The Architect's comments, notes or corrections are not an authorization to proceed with Work involving a change in the Contract Sum, the Contract Time or both. If any portion of this review requires a change to the Work, an appropriate change instrument must be executed in accordance with the Contract Documents.

DLR Group
Date: 3/15/2024
By: ibanerji

construction and fabrication. All work performed by the contractor shall be done in a satisfactory manner and coordinated with all other trades and existing conditions. Any corrections shown on these shop drawings and all work and products provided by the contractor are subject to the requirements of the plans and specifications.

N · FORM ARCHITECTURE, LLC

By: Jenine May Date: 9/12/2023

ARCHITECTURE



PARAGON
ARCHITECTURE

RESUBMIT



made on the submittal(s) during this review do not comply with the requirements of the drawings and general compliance with the information given in the Contract Documents. The contractor is responsible for: confirming and correlating all fabrication processes and technique of construction; coordinating his or her work with that of all the other trades, including but not limited to previously reviewed submittals, and performing all work in a safe and satisfactory manner. Unless noted otherwise, field verification of dimensions and verification of quantities are the responsibility of the contractor.

BY Alex Mosby DATE 2/18/2025

Change vs Clarification

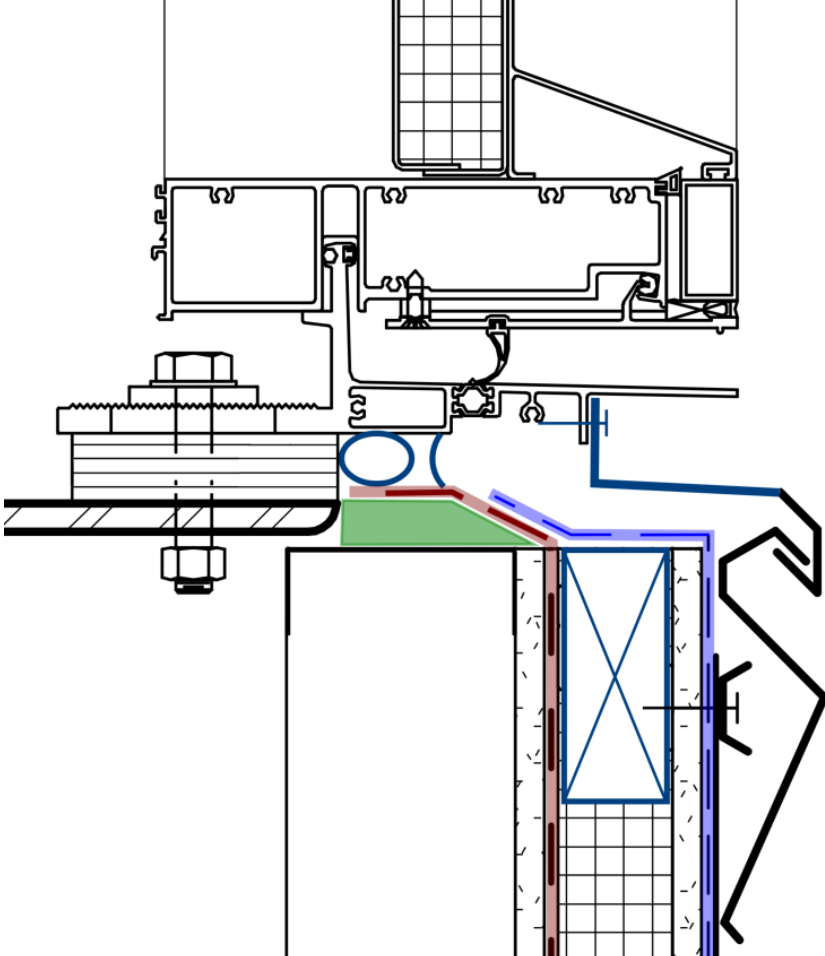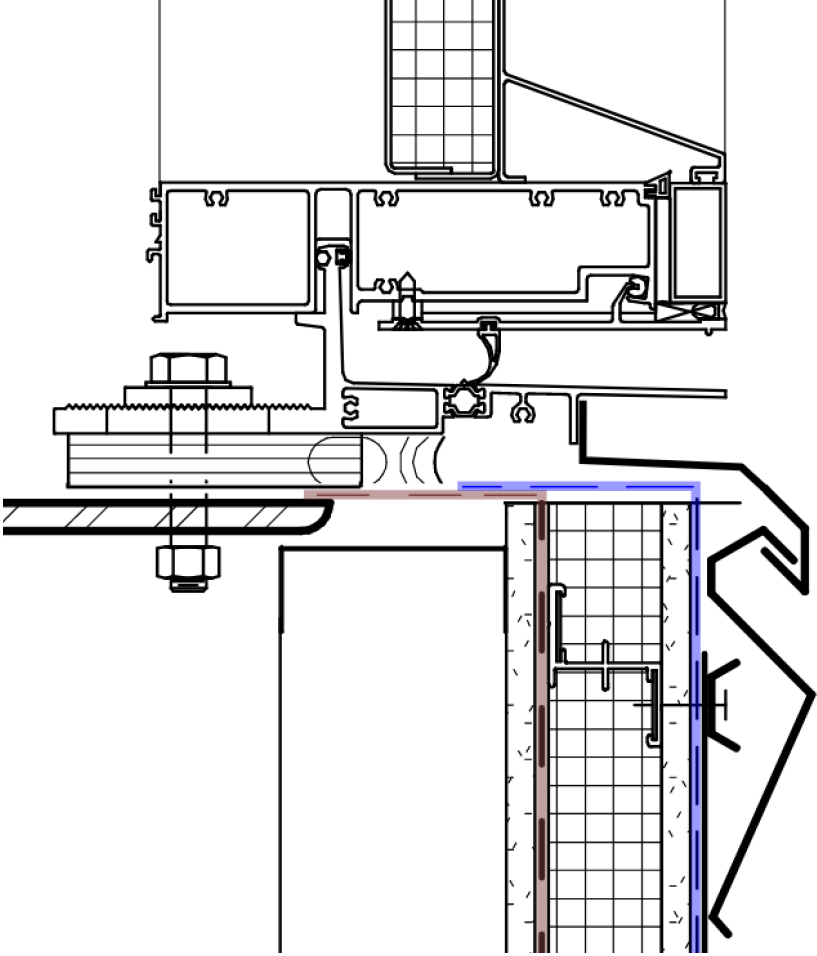

Change vs Clarification

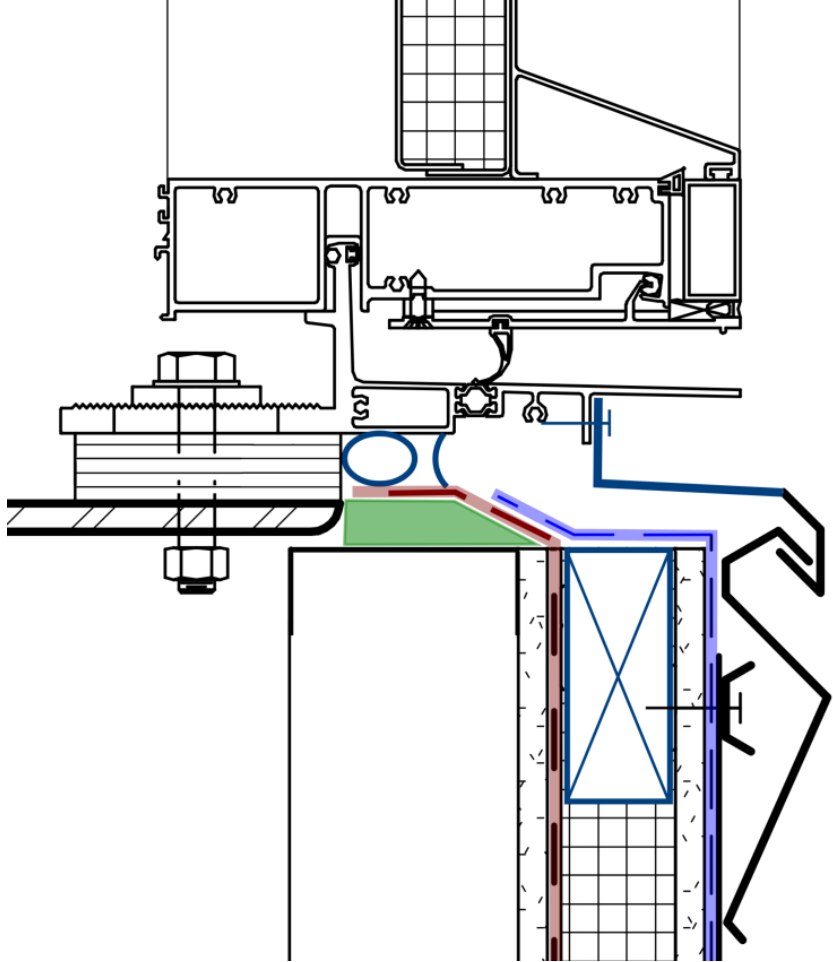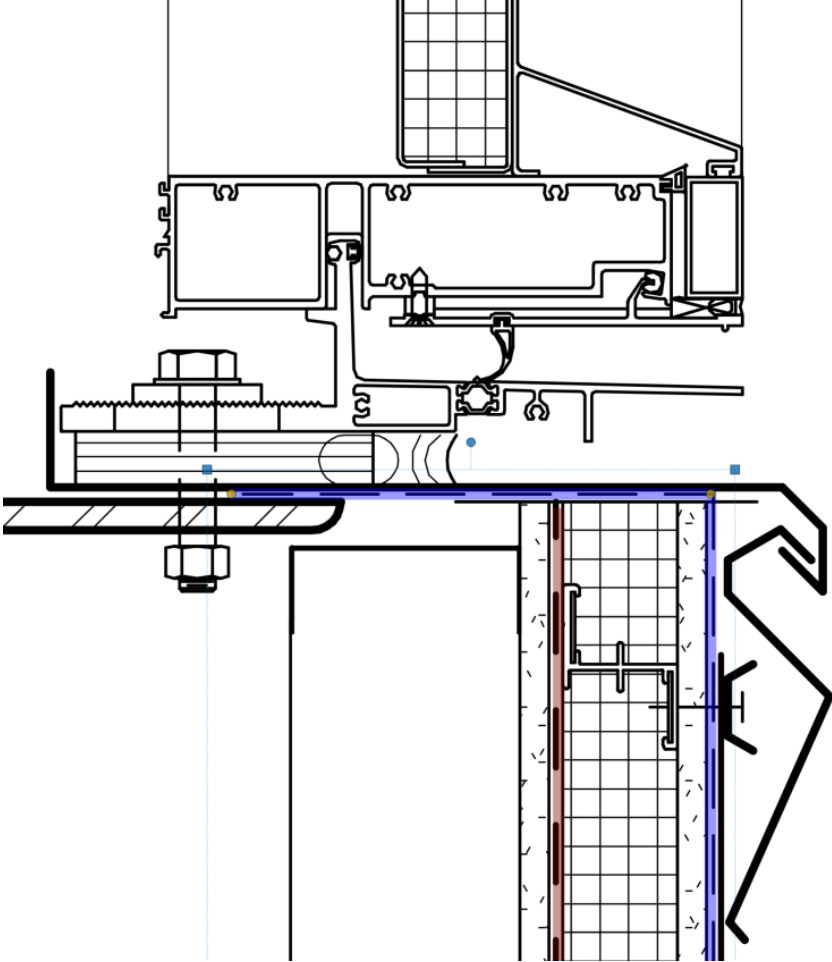



abaa2025 building
enclosure
conference

Thank You to Our
PLATINUM SPONSOR




Thank You to Our Sponsors & Partners




HIGH PERFORMANCE AIR & MOISTURE BARRIERS



technologies by 



BOARD OF DIRECTORS



Andrew Dunlap
AIA, CDT, LEED AP, NCARB
SmithGroup



Brian Stroik
FABAA, CABS
American Contractors Insurance
Group



John Posenecker
P.E.
Terracon Consultants, Inc.



Julie Szabo
CET, CABS
Wiss, Janney, Elstner Associates



Sarah K. Flock
NCARB, BECxP, CxA+BE
Raths, Raths & Johnson, Inc



Benjamin Meyer
AIA, NCARB, LEED AP
Siplast



Gilbert Alvarez
Alpha Insulation & Waterproofing
Inc.



Matt Nelson
P.E., LEED AP, BCxP, CEM
ECO Comissions



Andrea Wagner Watts
LEED Green Associate
GAF



Andre Desjarlais
OakRidge National Laboratory



Mike Bingley
BSA, AIA, NCARB
R.J. Kenney Associates,
Inc



Cody Shelner
CABS
Tesa tape/ Functional Coatings



Craig Wetmore
FABAA, CDT, EBS
York Flashings




Peter Barrett
BA, MBA
Dörken Systems Inc



John Chamberlin
BS, MBA
Georgia-Pacific Gypsum



Keith Nelson
NCARB, AIA, CDP, BCxP
DuPont Building Performance
Solutions



Matt Giambrone
CABS
OCP Contractors Inc



Adam Ugliuzza
P.E., CPHC
Sustainable Building Partners



Kevin Nolan
Vaproshield



Guy Long
PROSOCO



Amy Baker
AIA, LEED AP, CSI, CDT, SCIP
Amy Baker Architect



Scan to Download the App



Plan Your Day



Connect with Attendees



Ask Speakers Questions



Never Miss an Announcement



Win Prizes
